# Lab 2: Agile backlog creation & Sprint simulation in Jira

SRN: PES1UG24CS523

Name: Vedanth Kiran

Section: I

Project: Micro-Lending and Peer Credit Risk Assessor (Jira key: MLPCRA)

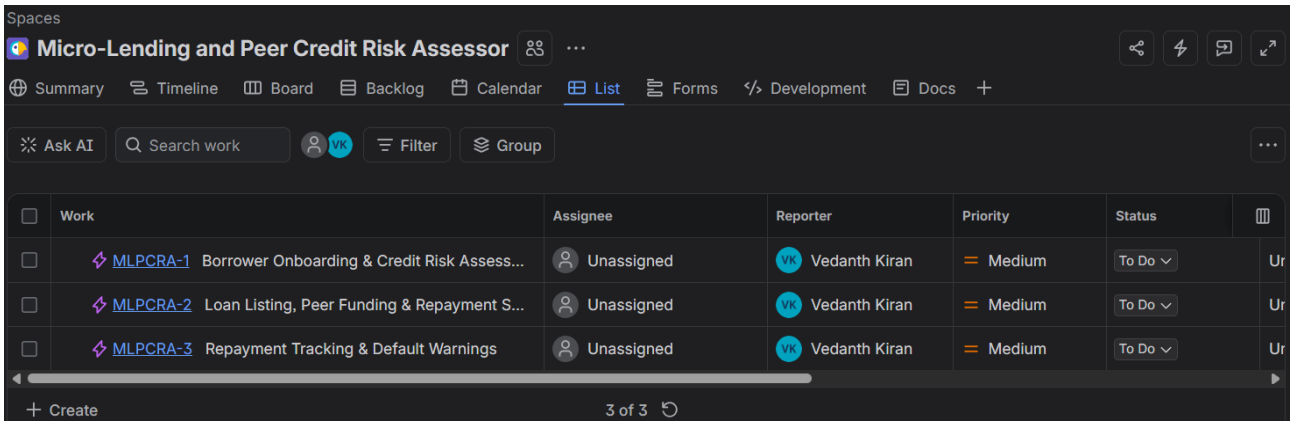
## Epics

| Key | Epic | Stories |
|---|---|---|
| MLPCRA-1 | Borrower Onboarding & Credit Risk Assessment | MLPCRA-4 to MLPCRA-7 |
| MLPCRA-2 | Loan Listing, Peer Funding & Repayment Schedule | MLPCRA-8 to MLPCRA-11 |
| MLPCRA-3 | Repayment Tracking & Default Warnings | MLPCRA-12 to MLPCRA-15 |

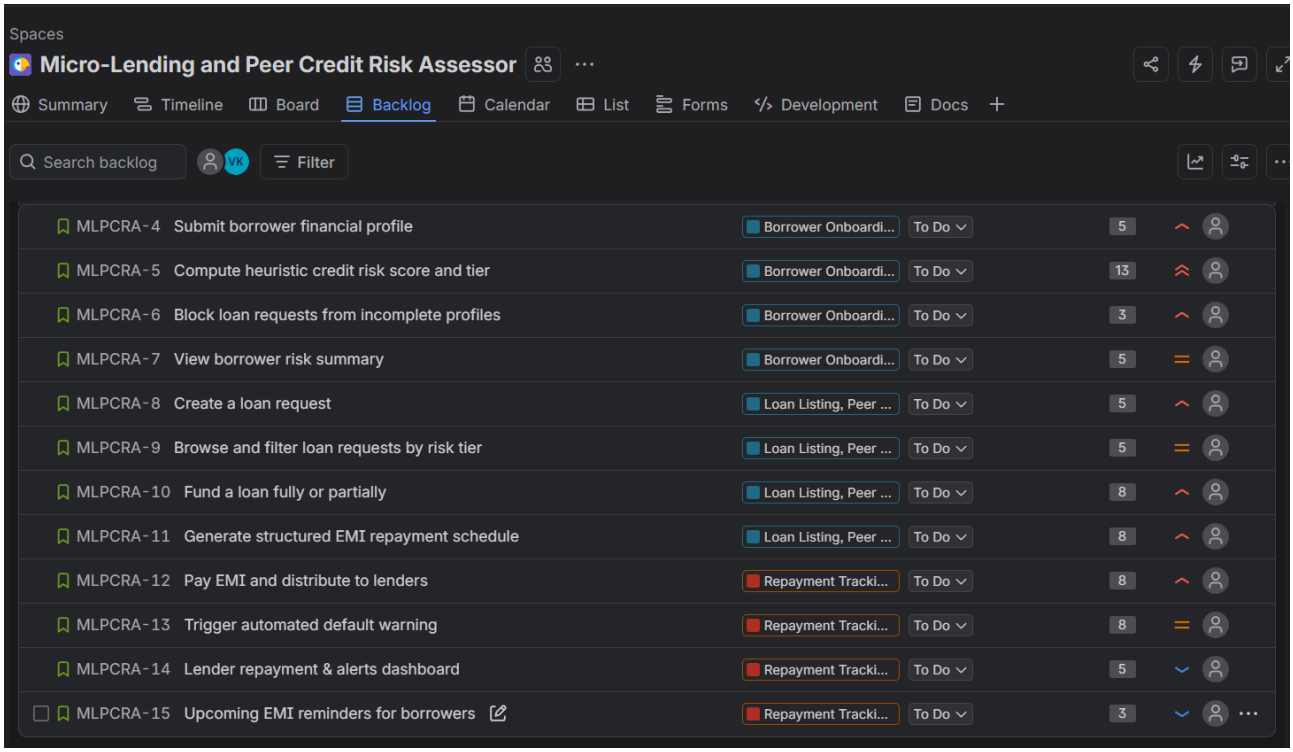
## User stories, priorities and story points

| Key | User story | Epic | Priority | Points |
|---|---|---|---|---|
| MLPCRA-4 | Submit borrower financial profile | 1 | High | 5 |
| MLPCRA-5 | Compute heuristic credit risk score and tier | 1 | Highest | 13 |
| MLPCRA-6 | Block loan requests from incomplete profiles | 1 | High | 3 |
| MLPCRA-7 | View borrower risk summary | 1 | Medium | 5 |
| MLPCRA-8 | Create a loan request | 2 | High | 5 |
| MLPCRA-9 | Browse and filter loan requests by risk tier | 2 | Medium | 5 |
| MLPCRA-10 | Fund a loan fully or partially | 2 | High | 8 |
| MLPCRA-11 | Generate structured EMI repayment schedule | 2 | High | 8 |
| MLPCRA-12 | Pay EMI and distribute to lenders | 3 | High | 8 |
| MLPCRA-13 | Trigger automated default warning | 3 | Medium | 8 |
| MLPCRA-14 | Lender repayment & alerts dashboard | 3 | Low | 5 |
| MLPCRA-15 | Upcoming EMI reminders for borrowers | 3 | Low | 3 |
|  | Total |  |  | 81 |

Jira backlog with Epics and User Stories. (Screenshot 1)

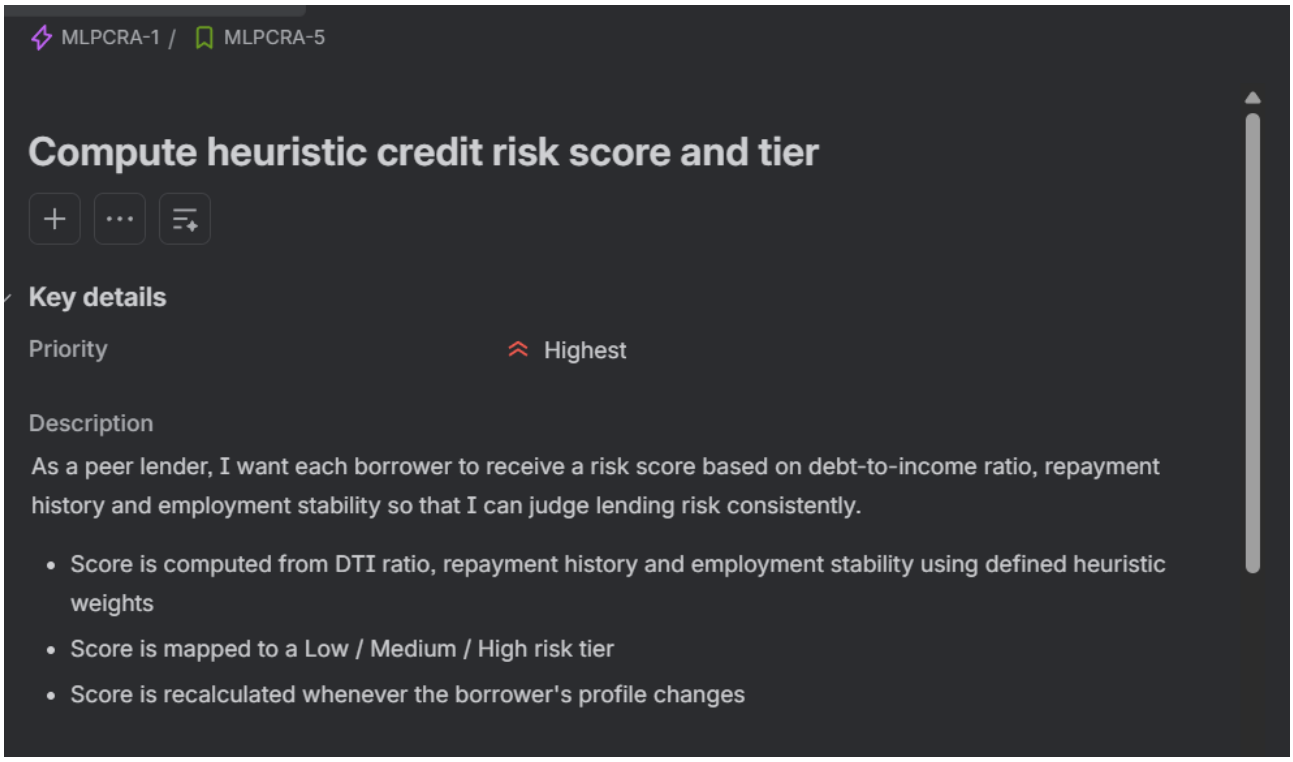



Epics created in the List view.



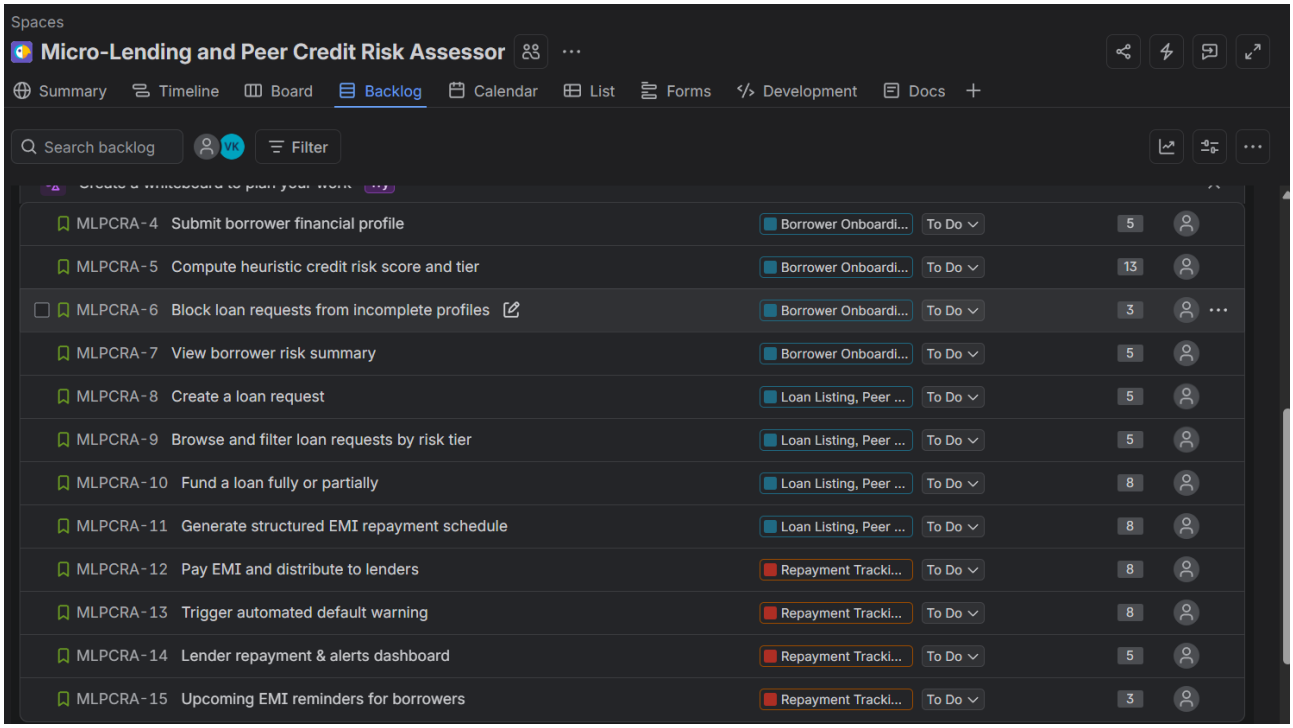

Backlog with all 12 user stories linked to their epics, with priorities.

Example user story.




MLPCRA-5 with user story description and acceptance criteria.


Story point assignments. (Screenshot 2)



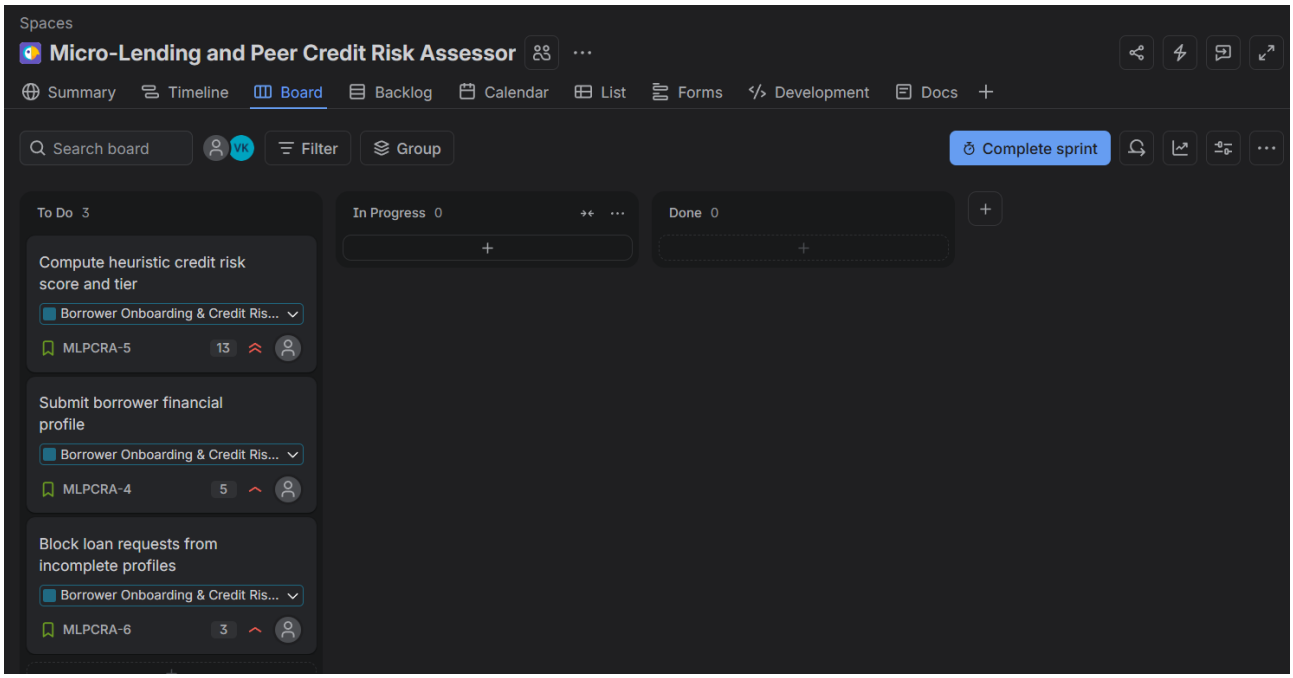

Story points estimated on the Fibonacci scale (3, 5, 8, 13). Total backlog: 81 points.

Sprint board (Active Sprint view). (Screenshot 3)

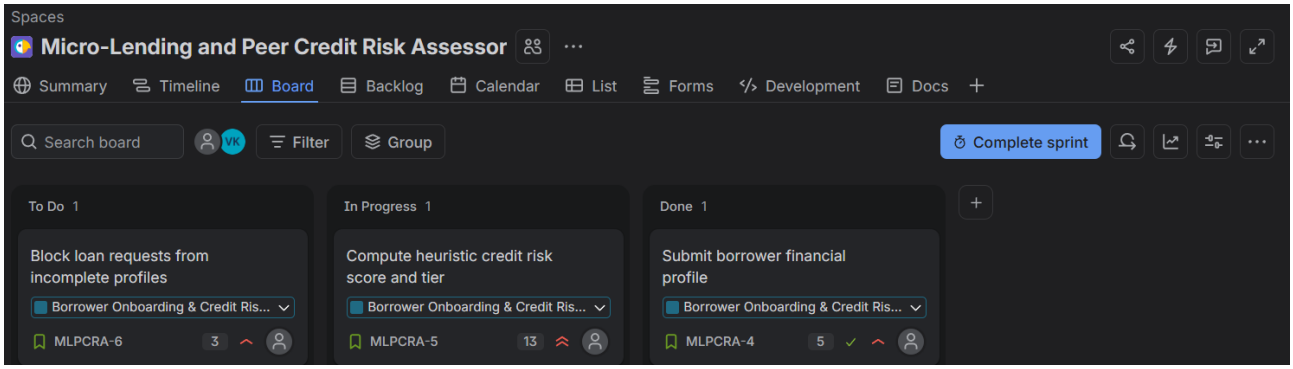
Sprint 1



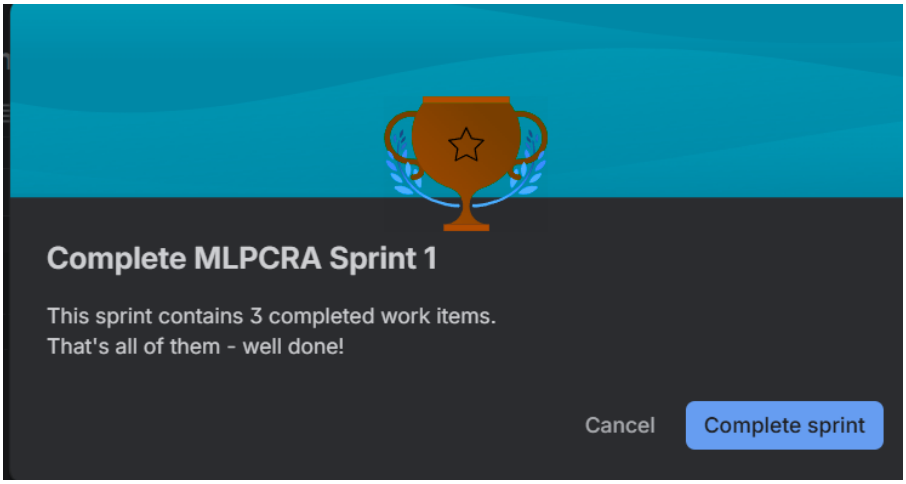

Sprint 1 planned with MLPCRA-4, 5 and 6 (21 story points).




Sprint 1 started - all items in To Do.



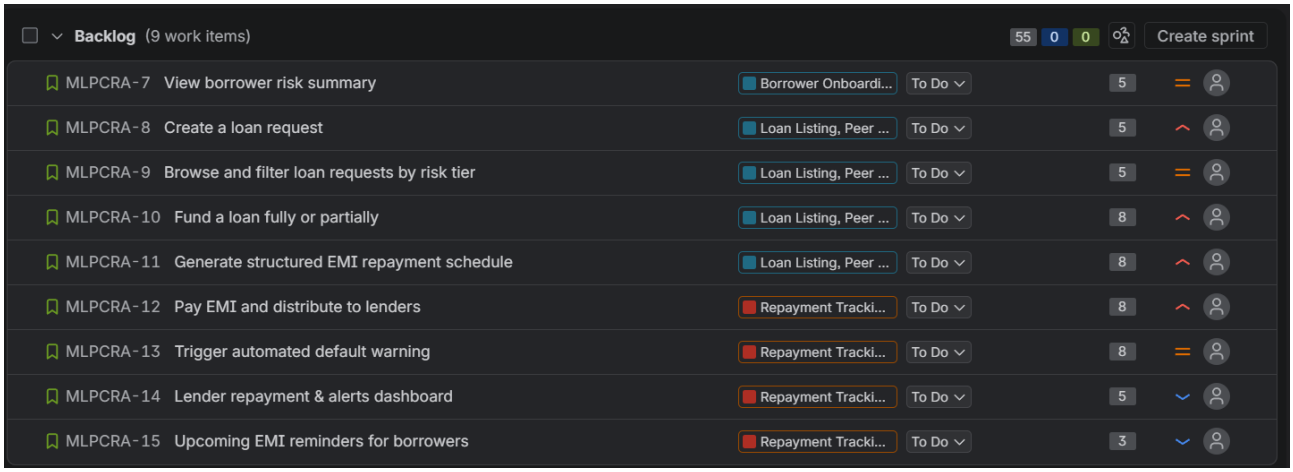

Sprint 1 in progress.





Completing Sprint 1 - all 3 work items done.

Sprint 2

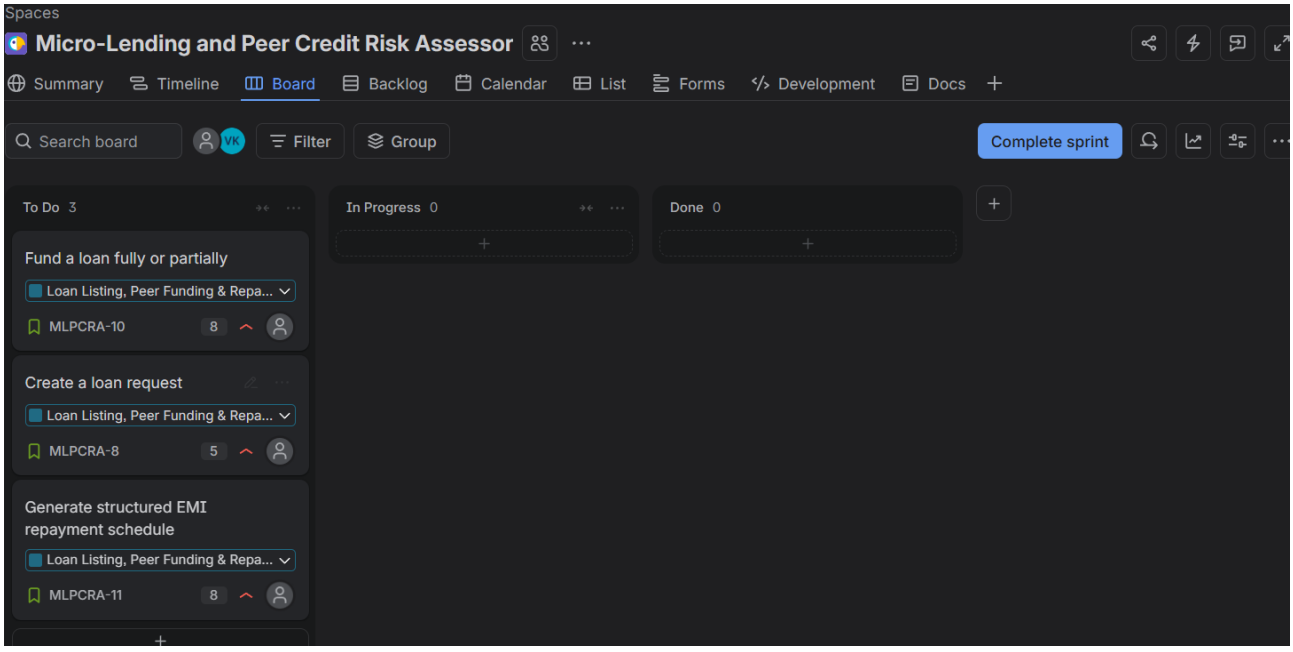
Remaining backlog after Sprint 1



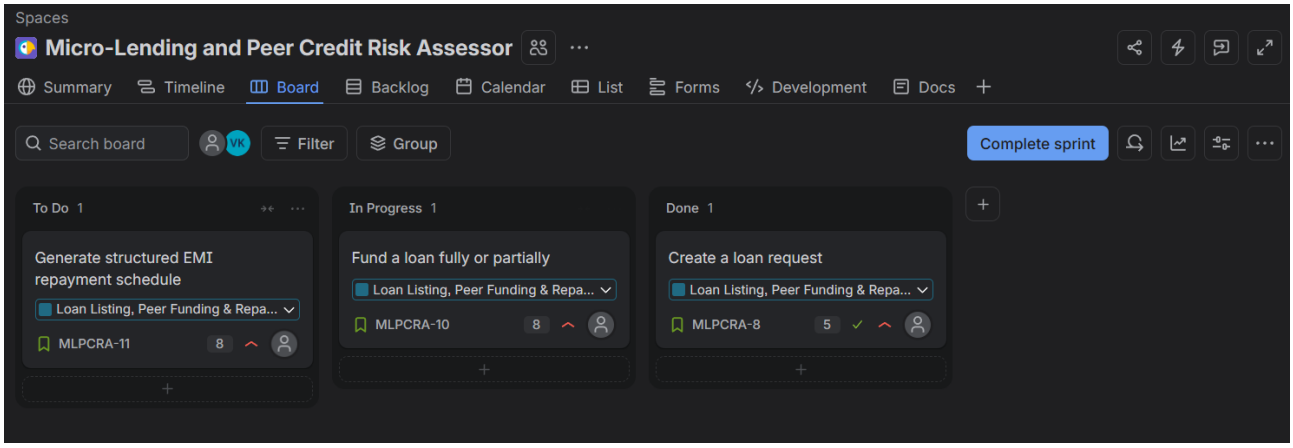

Backlog after Sprint 1: 9 work items, 55 story points remaining.



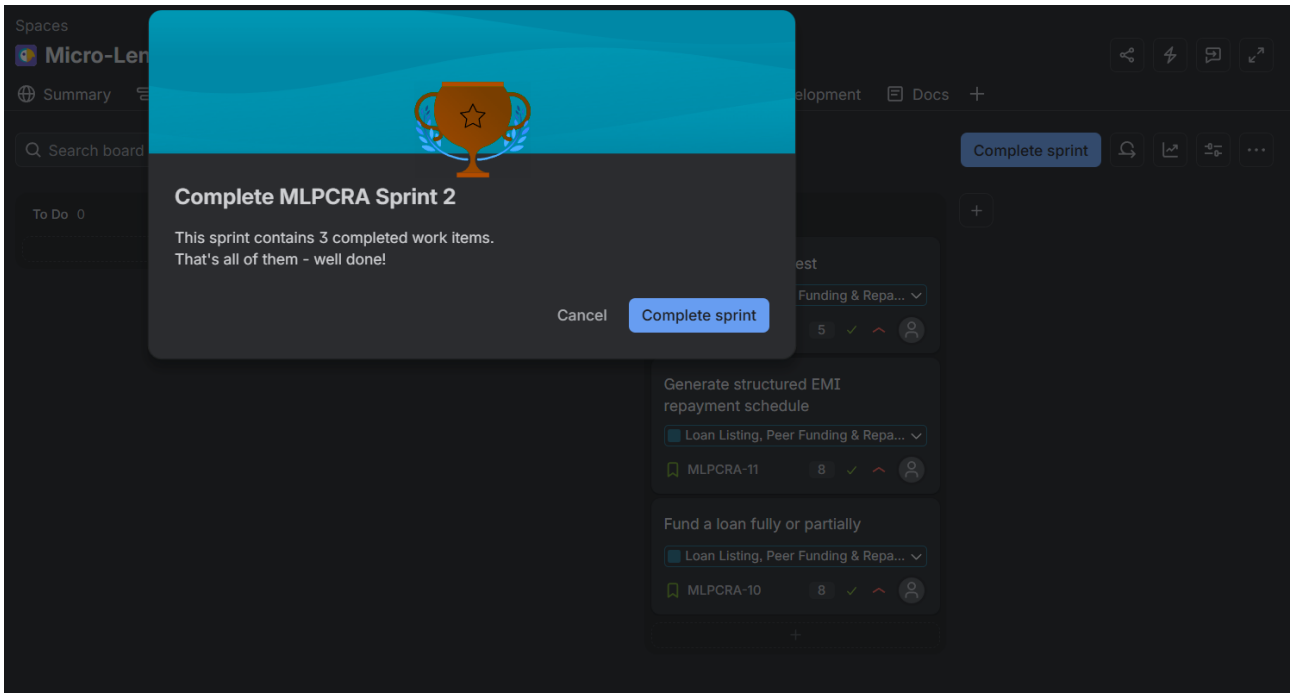

Sprint 2 planned with MLPCRA-8, 10 and 11 (21 story points).




Sprint 2 started - all items in To Do.




Sprint 2 in progress.




Completing Sprint 2 - all 3 work items done.

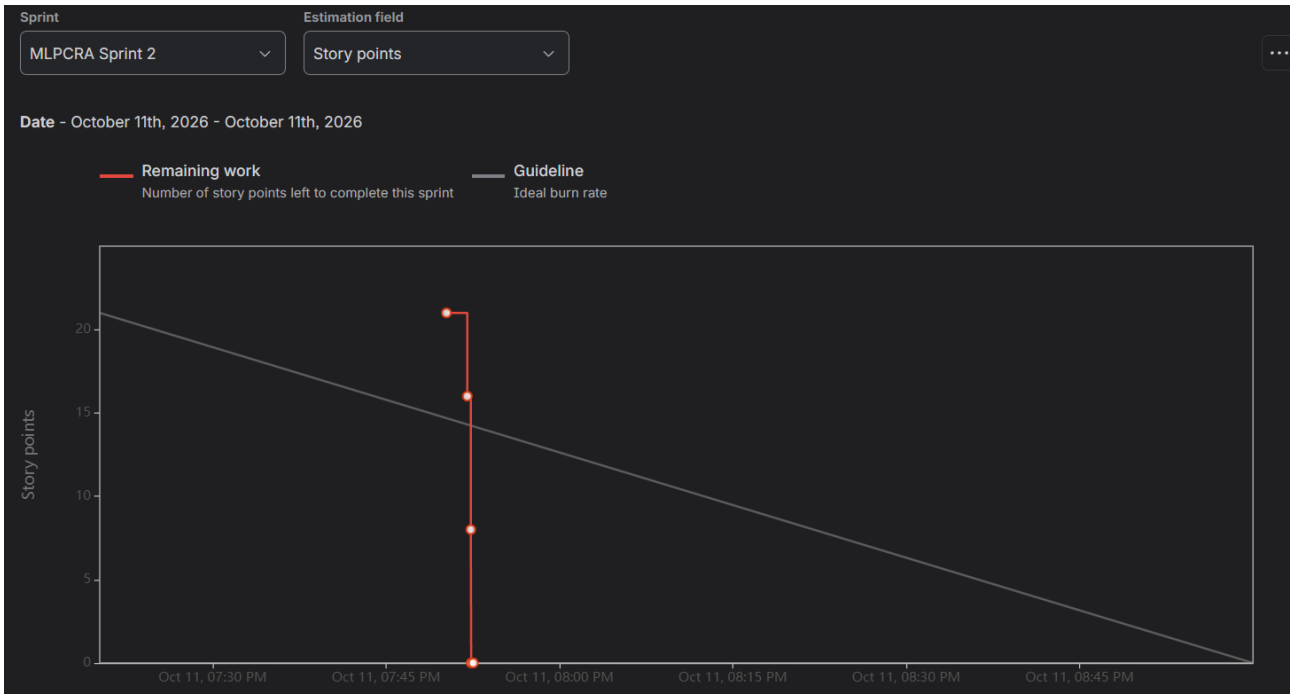
Burndown Chart. (Screenshot 4)

Sprint 1




Sprint 1 burndown: 21 to 16 (MLPCRA-4 done) to 0.

Sprint 2




Sprint 2 burndown: 21 to 16 (MLPCRA-8) to 8 (MLPCRA-10) to 0 (MLPCRA-11).

## Reflection Questions:

### 1. Did your estimations reflect the actual effort?

Broadly, yes. Relative sizes held up: the credit risk scoring story (MLPCRA-5, 13 points) involves defining scoring rules, weighting financial inputs and mapping scores to risk tiers, so it was clearly the largest item in Sprint 1, while blocking incomplete profiles (MLPCRA-6, 3 points) was a small validation rule. Because this was a simulation, the wall-clock time to move items to Done was much shorter than real development would take, so the estimates were validated in relative terms rather than in actual hours.

### 2. Was your backlog well-prioritized?

Yes. The backlog follows the natural dependency order of a lending platform. Credit risk scoring was marked Highest because every later feature (loan listing, filtering by risk tier, default warnings) depends on it. Core money-flow stories such as submitting a profile, creating and funding a loan, generating the EMI schedule and paying EMIs were High. Supporting features such as the risk summary, filtering and default warnings were Medium, and convenience features like the lender dashboard and EMI reminders were Low.

### 3. How did your simulated sprint align with your plan?

The sprints followed the plan. Sprint 1 delivered the borrower onboarding foundation (MLPCRA-4, 5, 6) for 21 points, and Sprint 2 was planned at the same capacity of 21 points with the High-priority funding stories (MLPCRA-8, 10, 11). Each sprint finished all committed items, so nothing spilled over. The remaining Medium and Low items (MLPCRA-7, 9, 12-15) stay in the backlog for future sprints, which keeps the highest-value, highest-dependency work first so it can be validated with users and iterated on.

### 4. What insights did the burndown chart give about your team's capacity?

The burndown showed remaining story points dropping from 21 to zero within each sprint, which indicates a velocity of about 21 points per sprint. With 81 points in total, the full backlog would need roughly four sprints at this pace. Since the simulation moved items quickly, the chart drops in sharp steps rather than following the guideline smoothly; in a real project, large drops like the 13-point story would suggest splitting big stories so progress is visible earlier.
